



16281 Baseline Ave.
Shakopee, MN 55379
952.445.3173

Closed Circuit Television Inspection

Customer	Pipe Segment Ref.	Upstream MH	Downstream MH	Size	Material	Total Length
City of Shakopee	ID59-ID72	ID72	ID59	10	Vitrified Clay Pipe	453.5

Surveyor's Name	Certificate Number	Street Address	Location Details
Joshua Blaisdell	04-8359	Canterbury Rd S	


Direction	Purpose	Weather	Date	Sewer Use	Length Surveyed
Downstream	Routine Assessment	Snow	11/20/2014	Sanitary	198.9

Additional Information


Shakopee 2014



AMH - Access Point - Manhole @ 0.0 ft.
Begin inspection.

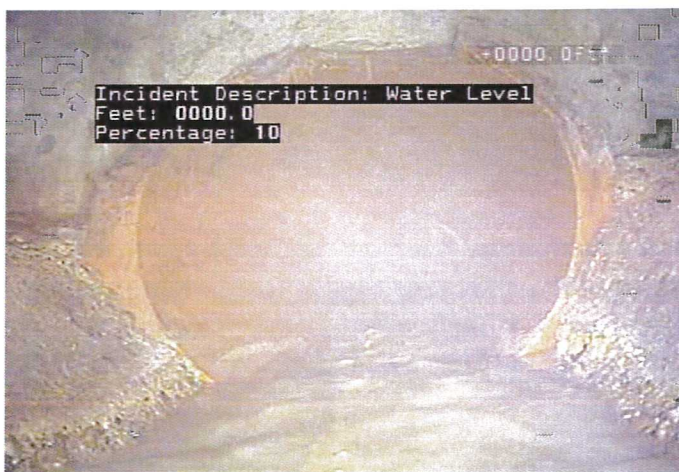


MWL - Water Level @ 0.0 ft.

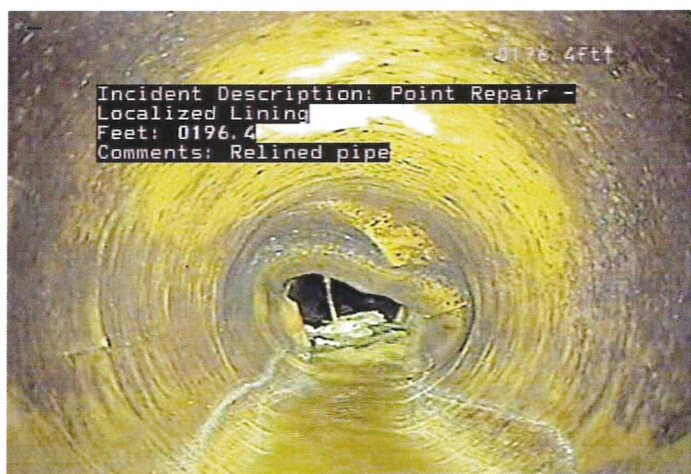


RPL - Point Repair - Localized Lining @ 194.3 ft. Relined pipe



D - Pipe Deformed @ 198.8 ft.

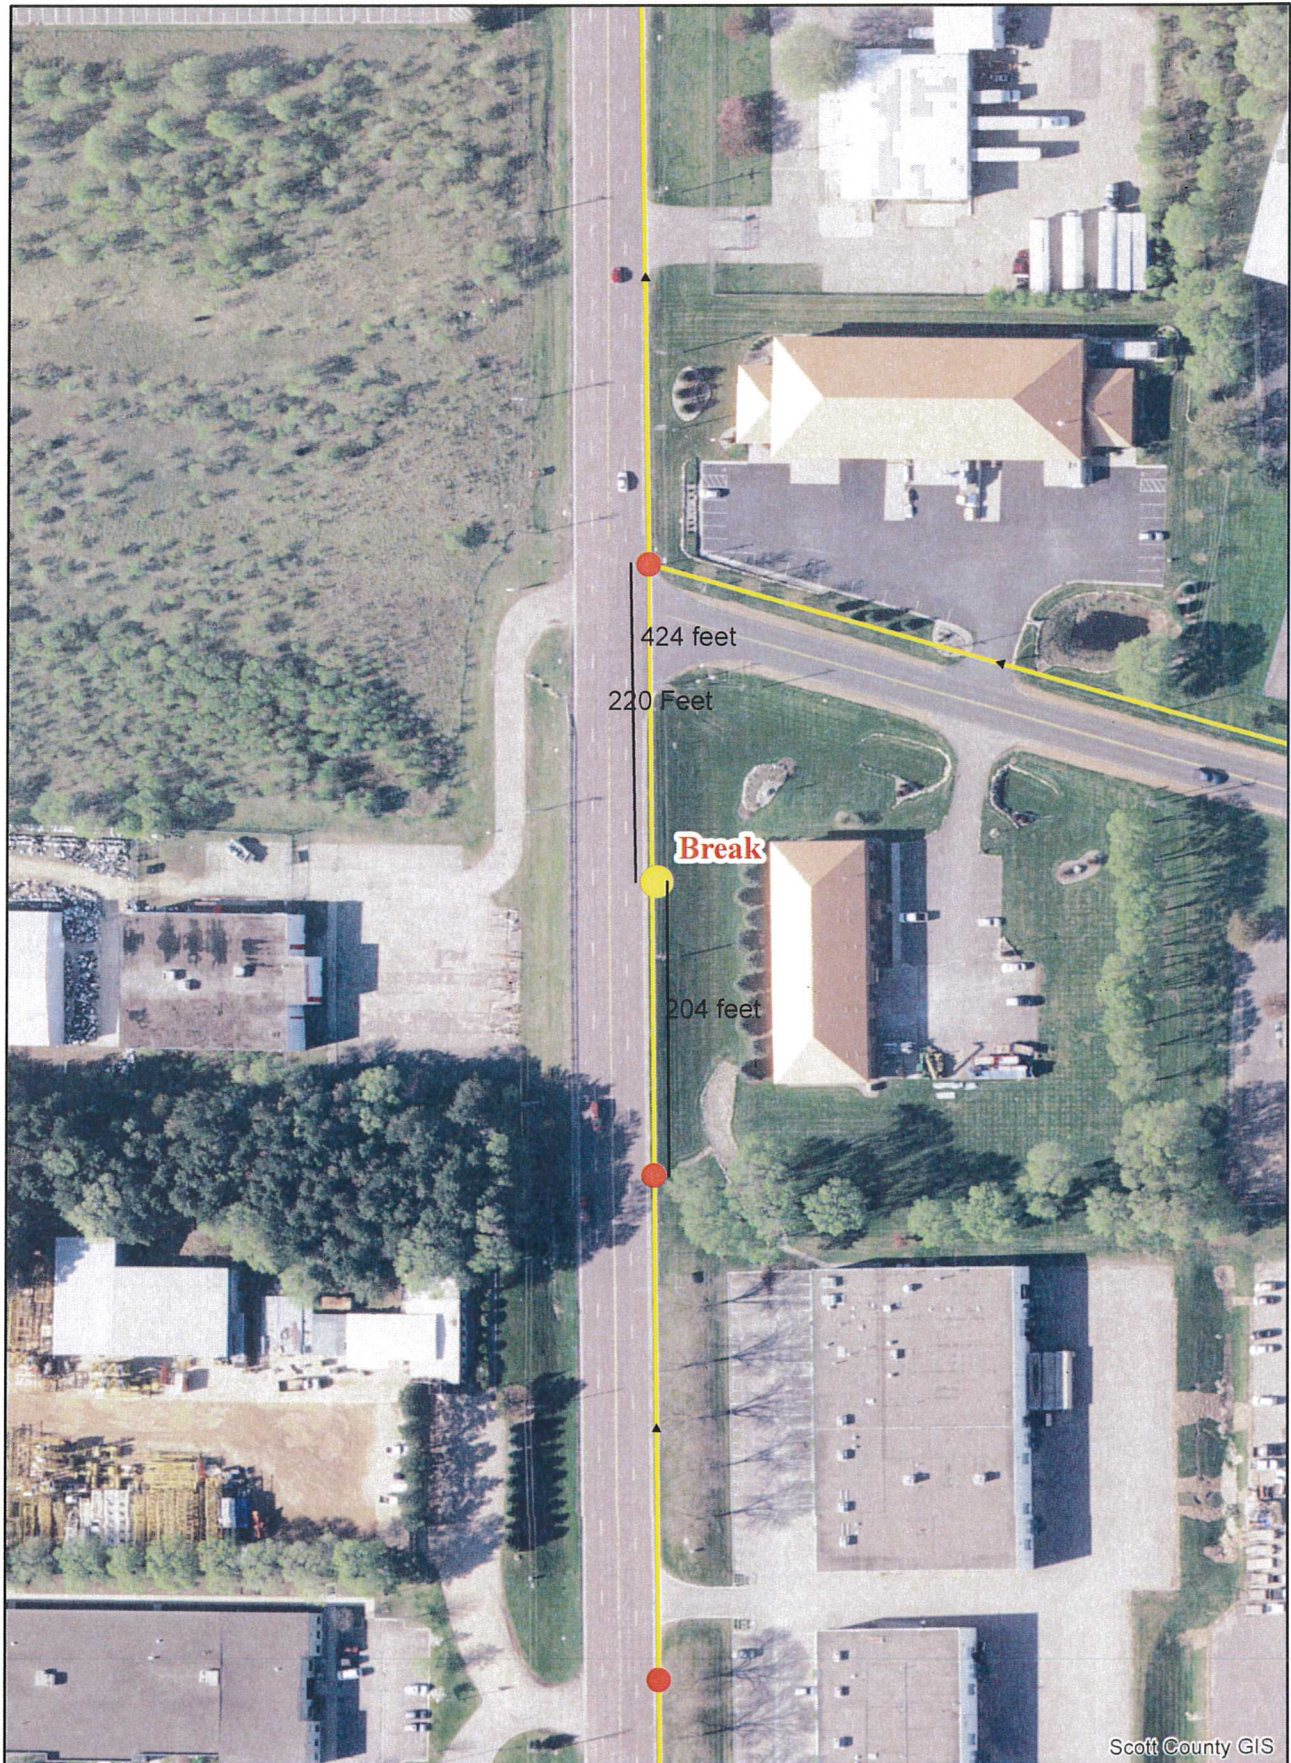



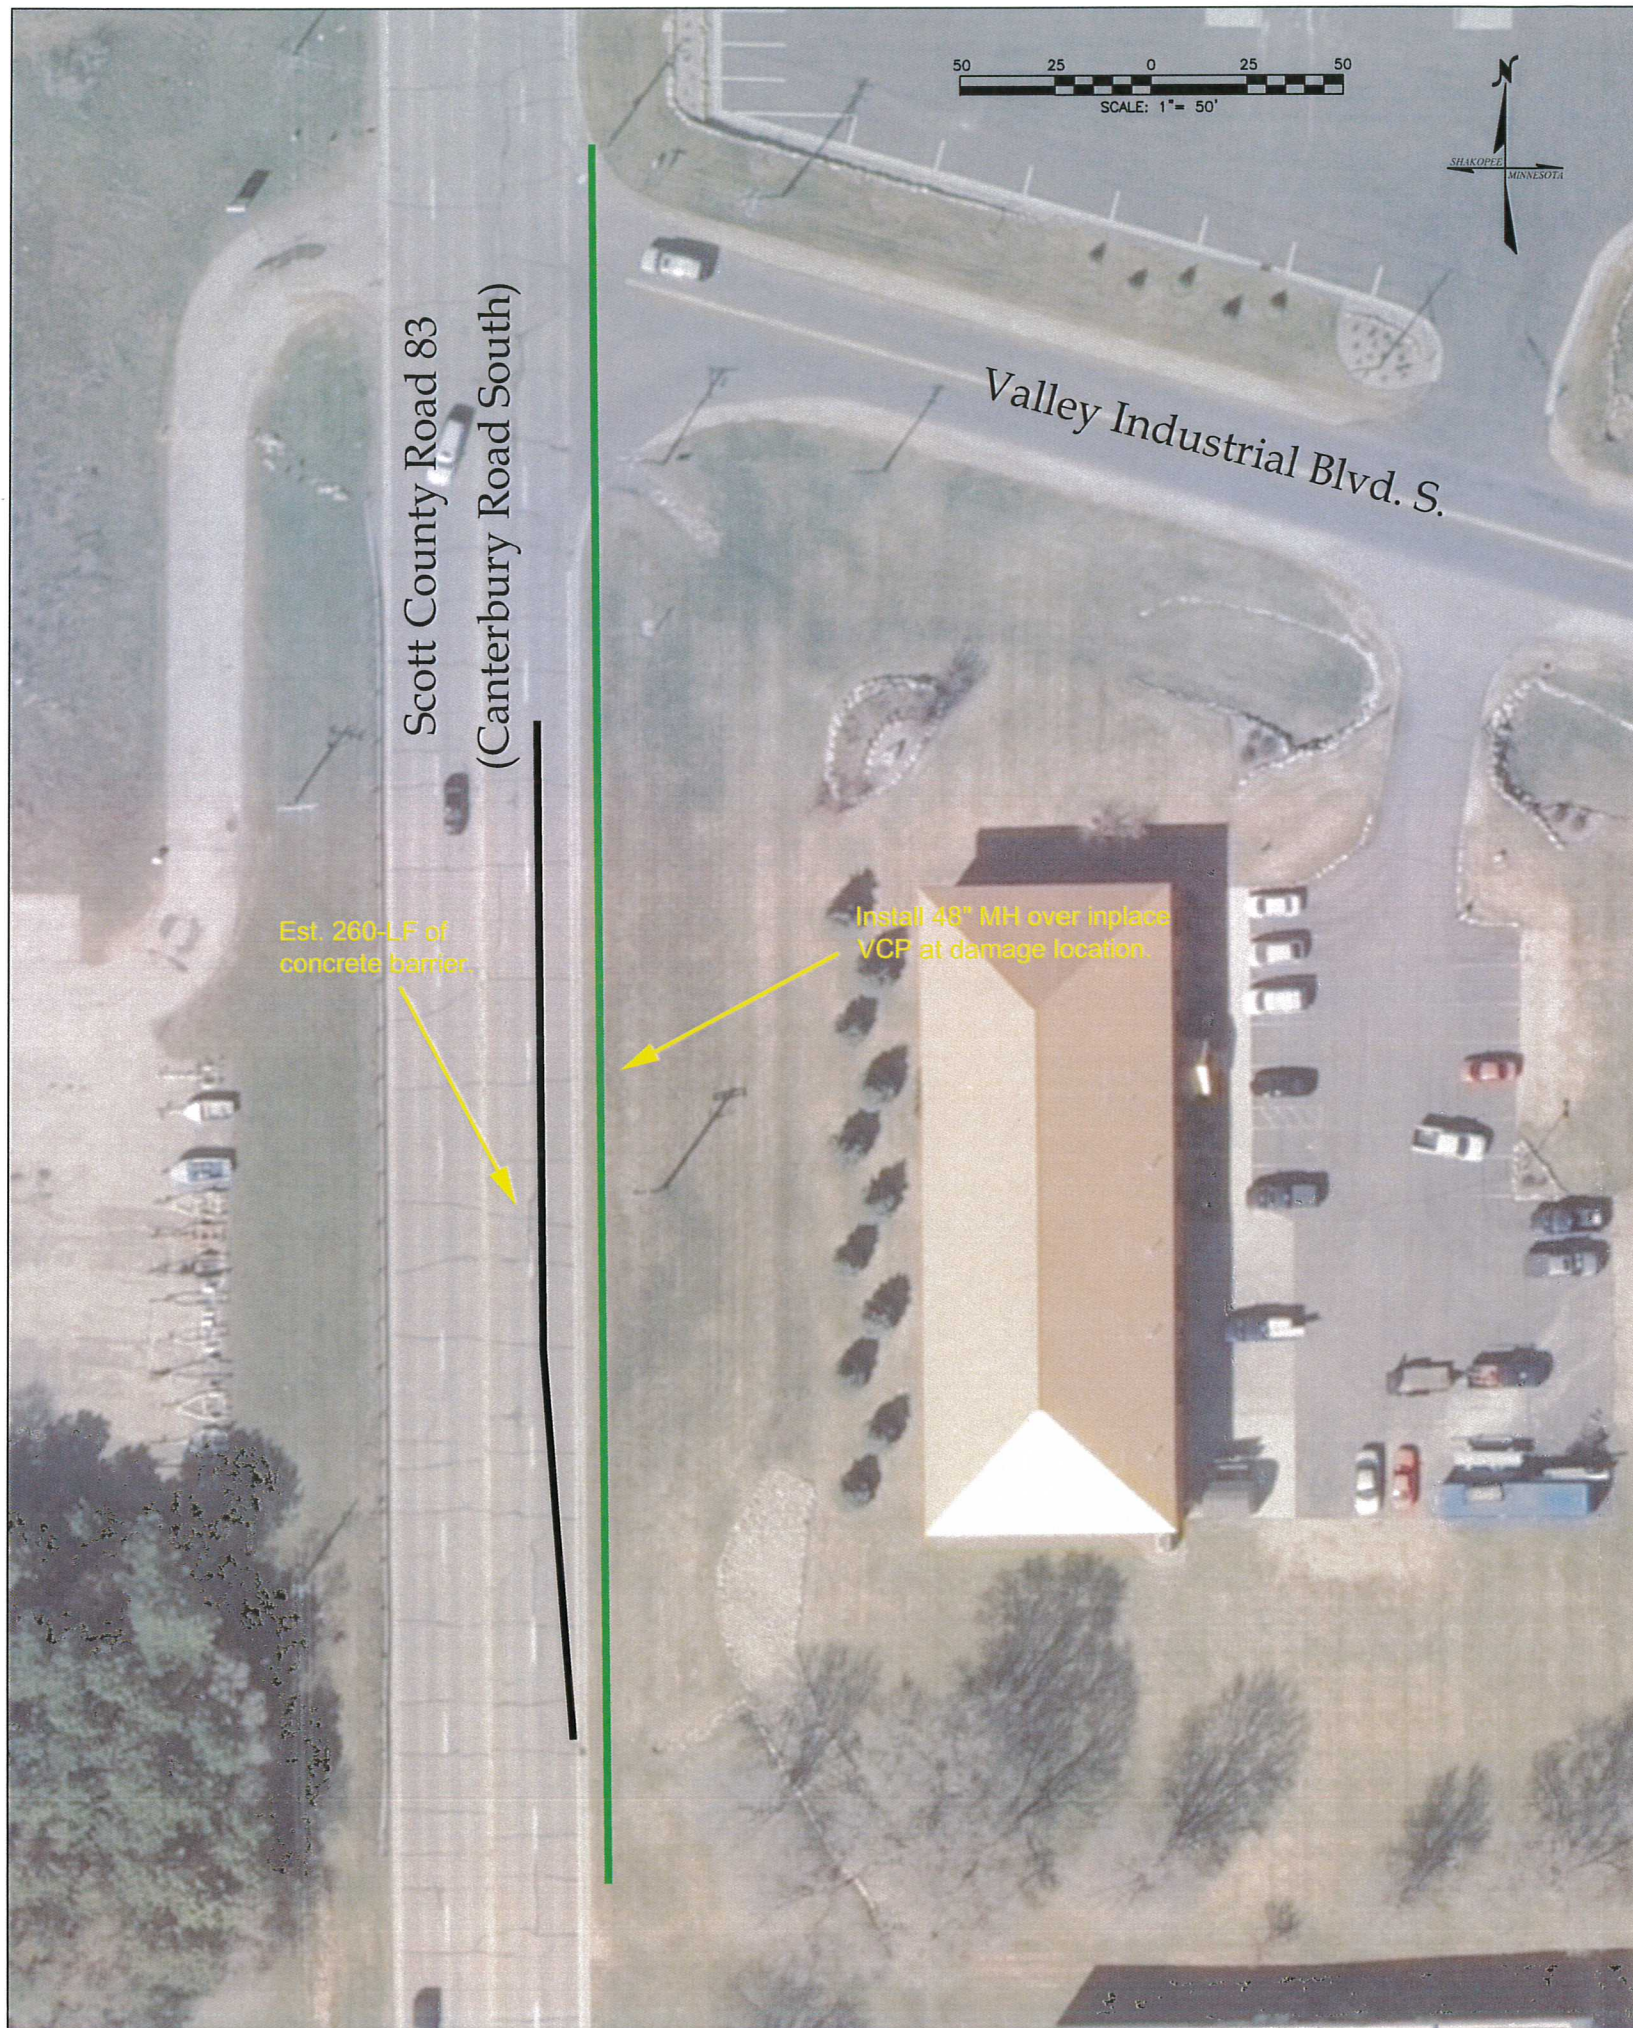

Sanitary Sewer Repair Project



Scott County Road 83 south of VIB-S

The project objective is to install a new 48" Manhole Structure over the in place 10"-VCP to repair a collapsing section with minimum disruption to traffic and the area around the work site. The city of Shakopee is requesting proposal for the work with all work to be complete on or before August 16, 2017. Proposal must include work plan, work dates, traffic-control plan, sub-contractors list and bid sheet. Please send your proposals to City of Shakopee, 400 Gorman St. S., Shakopee 55379 attn: Jim H. or email to JHenderson@ShakopeeMN.Gov by noon June 28, 2017. Please send all questions to Jim Henderson or call 952-233-9368 M-F 7-3.

Est. Bid items are:

- Mobilization (LS)
- Traffic Control (includes concrete barrier) (LS)
- Remove and Replace Curb (LF)
- Remove and Replace bituminous (includes class-V) (SY)
- Rock Excavation (est. 30-CY or less) (CY)
- 48" Manhole with casting (est. 16.5-LF) (LF)
- Top-soil and sod for restoration (LS)

** All other items are incidental to the project.

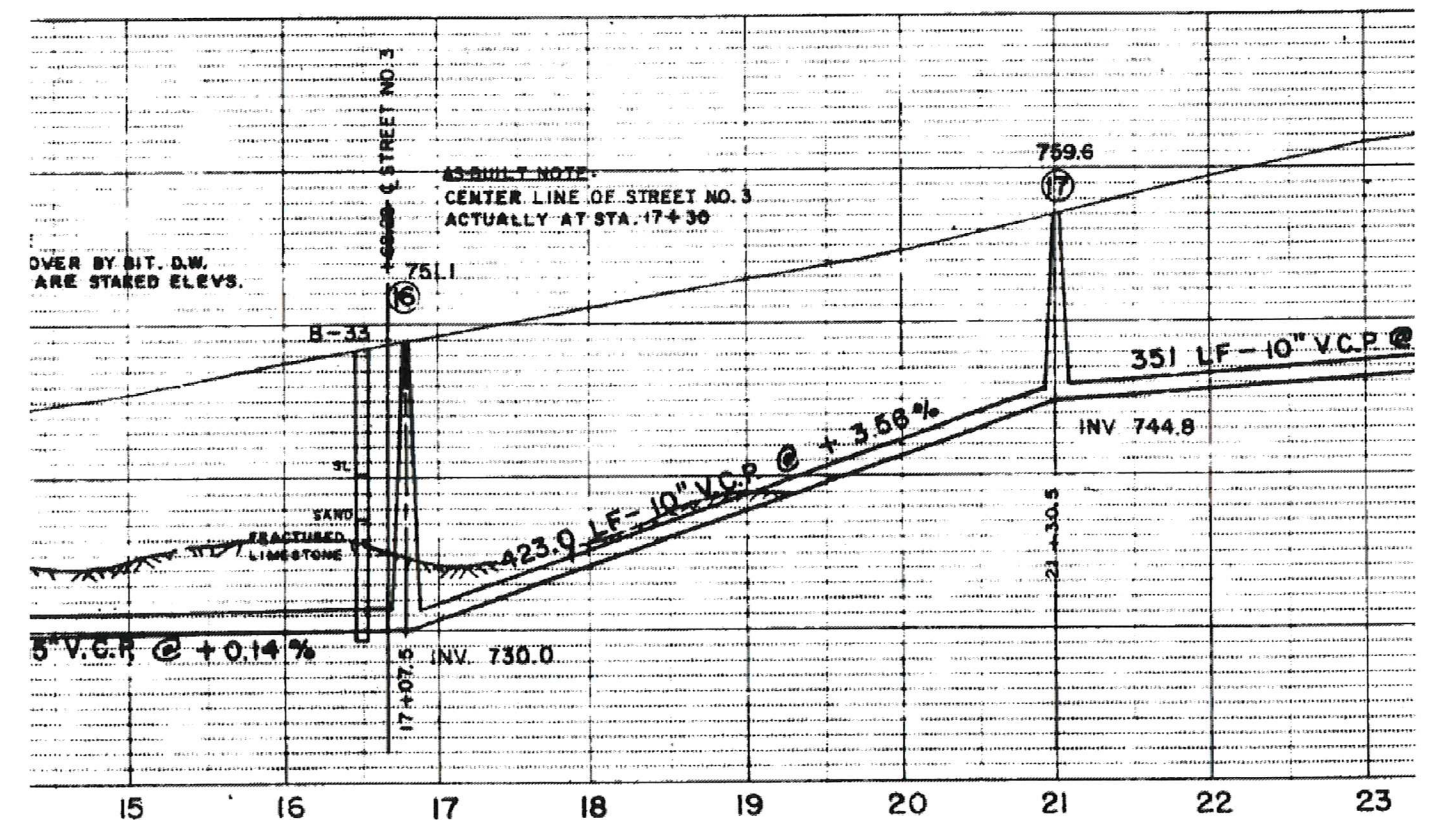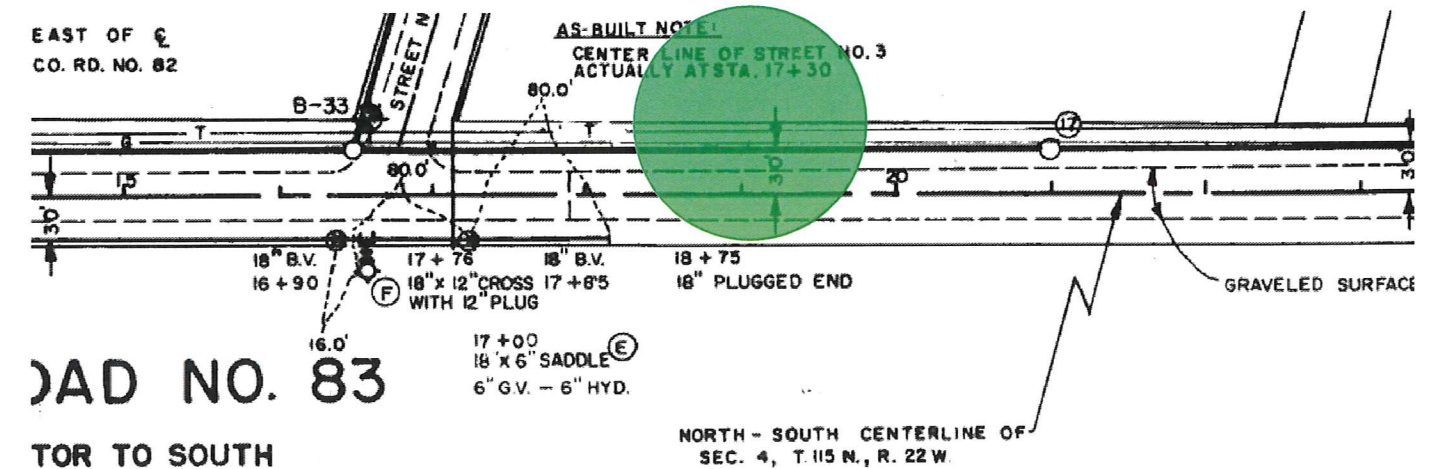

PARROTT CONTRACTING, INC.

30090 STATE HWY 93

HENDERSON MN 56044

507-248-9697 Office / 507-248-9655 FAX

dparrott@frontiernet.net

ESTIMATE

PROPOSAL SUBMITTED TO: City of Shakopee – Jim Henderson

JOB NAME: Canterbury Rd Sanitary Sewer Repair

ADDRESS: Shakopee, MN

DATE: June 28, 2017

We hereby submit as per conversation and outlined below:

Estimated cost to install 48" x 18' manhole on Canterbury Rd

Includes: traffic control, restoration of turf, curb & asphalt

ESTIMATED COST: \$40,000-\$45,000.00

Prices do not include any costs for: WAC & SAC fees, special licenses, state review or permit(to be done by others), dewatering, frost ripping, bond or share of bond, final adjustment of structures (to be done by others), construction staking, engineering fees or testing unless otherwise states above. We are not responsible for root damage to trees or irrigation system repairs. Property owner is responsible for locating any privately owned utilities on the property such as but not limited to, irrigation, gas, electric, etc.

Parrott Contracting hereby proposes to furnish labor and materials – complete in accordance with above specifications, for the sum of see above(\$see above) with payment to be made as follows: 30 days following completion late charges at 1.5% p/month.

All material is guaranteed to be as specified. All work to be completed in a workmanlike manner according to standard practices. Any alterations for deviation from above specifications involving extra costs, will be executed only upon written orders, and will become an extra charge over and above the estimate. All agreements contingent upon strikes, accidents, or delays beyond our control. This proposal is subject to acceptance within 10 days of bid opening or date of proposal and is void thereafter at the option of the undersigned.

AUTHORIZED SIGNATURE _____ DATE _____

ACCEPTANCE OF PROPOSAL

The above prices, specifications and conditions are hereby accepted. You are authorized to do the work as specified. Payment will be made as outlined above.

AUTHORIZED SIGNATURE _____ DATE _____



Specialty Contracting & Waste Management

14000 Veit Place
Rogers, MN 55374-9583

Office 763.428.2242
Fax 763.428.8348

VeitUSA.com

June 20, 2017

To: City of Shakopee
Attn: James Henderson
Project: Sanitary Manhole Installation

Utilities (No Drawings Provided)

\$ 112,888.00

INCLUDES:

- 1 Mobilization
- Traffic Control
- Concrete Barriers
- Remove existing bituminous and curb
- Sanitary Bypass
- Remove 10-15 LF of crushed pipe
- Shoring using slide rail system
- Install 48" Manhole & backfill
- Place class 5, curbing & bituminous
- Grass restoration
- Rock Excavation (budget 40 CY)

EXCLUSIONS:

- Bond
- ALL permits
- Utility Inspections
- Soil Testing
- Soil Correction
- Mass Dewatering
- Winter Conditions/Frost Protection
- SWPPP Inspections
- Survey/Layout
- Utility/Areal Relocation
- Manhole Coatings/Dampproofing

Add 1% to Above Quoted Amount for Bond / Pricing Valid for 30 Days

Thank you for the opportunity
Respectfully submitted,

Jeff Carlson
Estimator
Veit & Company, Inc.
Cell: 612-490-7220
Direct: 763-428-6715

[Jcarlson1@veitusa.com](mailto:jcarlson1@veitusa.com)

Affirmative Action Equal Opportunity Employer

Contracting

Earthwork
Demolition
Utilities
Foundations
Environmental Remediation
Industrial Cleaning

Waste Management

Roll-off Containers
Construction & Demolition Debris Landfills
Recycling & Transfer Facilities
Waste Hauling
